

**McMILLAN PAZDAN SMITH**

**WCI GROUP LLC**

FIELD REPORT

<b><u>PROJECT:</u></b>	Leavelle McCampbell Middle	<b><u>FIELD REPORT NO.:</u></b>	One Hundred-Eleven (111)
<b><u>CONTRACT:</u></b>	Construction Management @ Risk HG Reynolds	<b><u>ARCHITECTS PROJECT NO.:</u></b>	

Review testing log and inspection reports  
 Fire Sprinkler- Main Drains Test date and other report dates needed in today.  
 Fire alarm is UL Certificate System.

- 7) Architect developed punch list during walk thru highlight OSF comments and concerns. There were several above ceiling items, including open boxes and or wire fastenings during inspection. GC site and coordination scope of work will satisfy Architects MPS/OSF punch list work required for final OSF sign off.
- 8) Exit Door Hardware to kitchen Label. Architect to clarify what’s needed. Change required. Mark floor at hood to assure equipment doesn’t exceed hood limitation.
- 9) Kitchen Hood Smoke test. Open Box above hood found by inspection. Box sealed at time of inspection. Support wire has been cut and trans cable
- 10) Stage storage opposite walls 2 & 3 hr walls
- 11) 3 type twist @ lights about ceiling are not correct
- 12) Storage handrails and stair treads and riser unfinished.

**SUBMITTALS:**

- 1) PVC Pediment-Resubmitted
- 2) RONCO re-submittal

**COORDINATION:**

N/A


**INSPECTIONS:**

- 1) NONE

**DEFICEINT WORK**

- 1) Architects “Punch List”
- 2) Refer to OSF inspection comments.
- 3)

**PHOTOS:** Attached

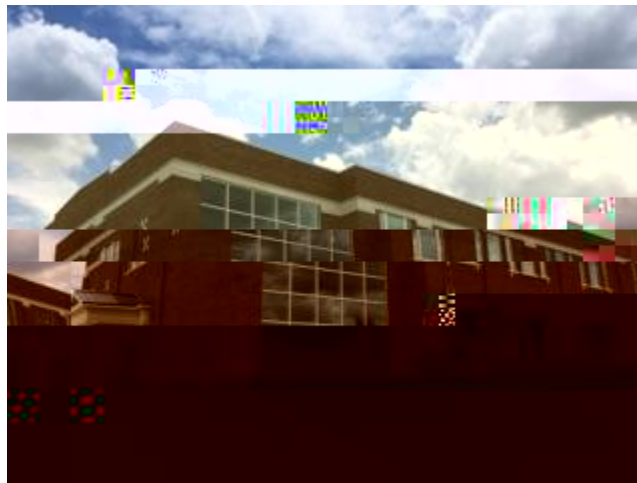

Drive around student drop off view (Typ.)

FIELD REPORT


---

<b><u>PROJECT:</u></b>	Leavelle McCampbell Middle	<b><u>FIELD REPORT NO.:</u></b>	One Hundred-Eleven (111)
<b><u>CONTRACT:</u></b>	Construction Management @ Risk HG Reynolds	<b><u>ARCHITECTS PROJECT NO.:</u></b>	

---



Campus landscape installation as exterior work is complete

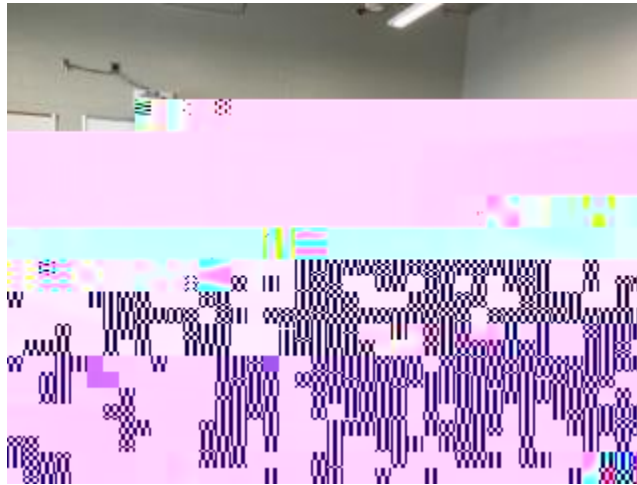


Typical Classroom set up as contractor complete  
Architects punch list

FIELD REPORT

---

<b><u>PROJECT:</u></b>	Leavelle McCampbell Middle	<b><u>FIELD REPORT NO.:</u></b>	One Hundred-Eleven (111)
<b><u>CONTRACT:</u></b>	Construction Management @ Risk HG Reynolds	<b><u>ARCHITECTS PROJECT NO.:</u></b>	

---

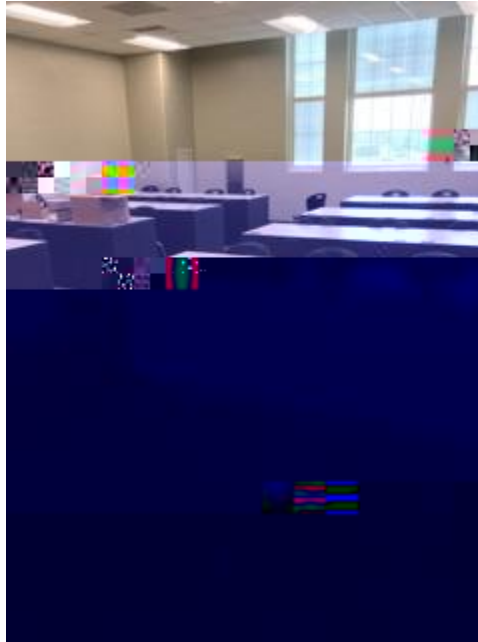

Classroom Typical finish flooring as carpet complete and furniture setup ongoing (Typ)



Common stairs with finishes applied (Typ)

FIELD REPORT

---

<b><u>PROJECT:</u></b>	Leavelle McCampbell Middle	<b><u>FIELD REPORT NO.:</u></b>	One Hundred-Eleven (111)
<b><u>CONTRACT:</u></b>	Construction Management @ Risk HG Reynolds	<b><u>ARCHITECTS PROJECT NO.:</u></b>	

---



Smart board installed and walls trimmed to complete (Typ)




Concession and wall display complete.

FIELD REPORT

---

<b><u>PROJECT:</u></b>	Leavelle McCampbell Middle	<b><u>FIELD REPORT NO.:</u></b>	One Hundred-Eleven (111)
<b><u>CONTRACT:</u></b>	Construction Management @ Risk HG Reynolds	<b><u>ARCHITECTS PROJECT NO.:</u></b>	

---

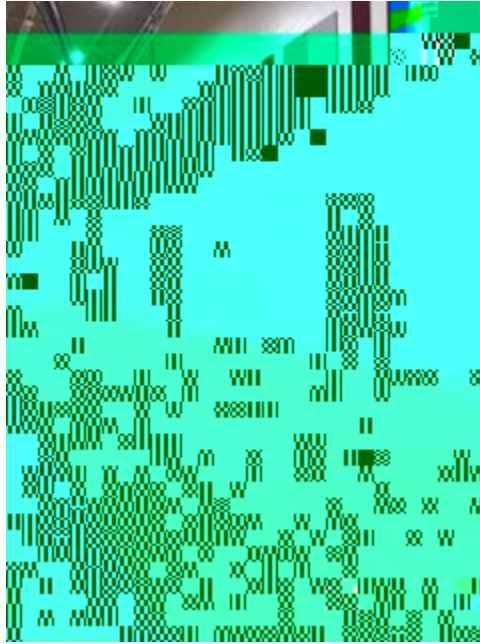

Typical Sound Batts placed and design consistent



See Gymnasium sound batts installed on perimeter wall

Report by: Wayne Jr. -WCI Group
