

FIELD REPORT

PROJECT: Leavelle McCampbell Middle **FIELD REPORT NO.:** Eighty-Six (86)

CONTRACT: Construction Management @ Risk **ARCHITECTS**
HG Reynolds **PROJECT NO.:**

FIELD REPORT

PROJECT: Leavelle McCampbell Middle **FIELD REPORT NO.:** Eighty-Six (86)

CONTRACT: Construction Management @ Risk **ARCHITECTS**
HG Reynolds **PROJECT NO.:**

- 12) Classroom cabinetry installation is consistent with plans and specifications.
- 13) HJR applied (4) coats of paint with required block filler as required. As paint continues to progress. Contractors masonry veneer is 100% complete as point up and clean up continues
- 14) Area scope of work by all trades are moving continuous and aggressively as required above ceiling inspections are consistent as coordinated by Contractor thru WCI and CCI.
- 15) Contractor has tentatively scheduled OSF Above Ceiling Inspection be for mid to late January 2017.

SUBMITTALS:

- 1) Submission is in progress. Includes Signage, Stucco, and flooring logos.
- 2) Canopy Re-submittals

COORDINATION:

- 1) Bi-weekly meeting Tuesday 10:00 am, January 9, 2016.
- 2) OSF coordination of inspection in mid to late January 2017.


INSPECTIONS:

- 1) Coordination scheduled by WCI Group
- 2) OSF coordination of inspection in mid to late January 2017.

DEFICEINT WORK:

- 1) None

PHOTOS: Attached

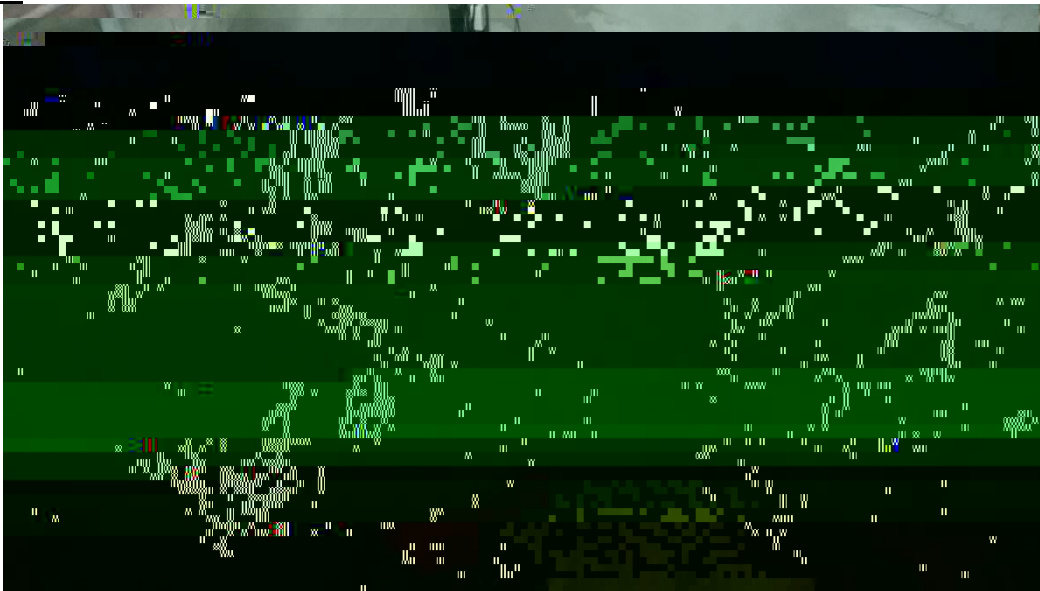

Sump pump pit for elevator is complete and ready for elevation assembly.



FIELD REPORT

PROJECT: Leavelle McCampbell Middle

FIELD REPORT NO.: Eighty-Six (86)

CONTRACT: Construction Management @ Risk
HG Reynolds

ARCHITECTS
PROJECT NO.:

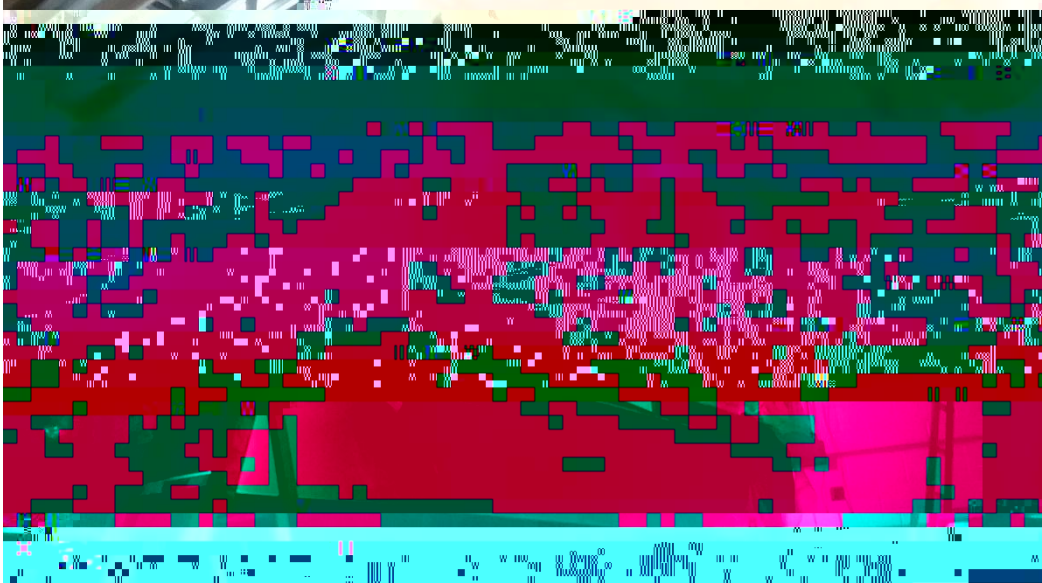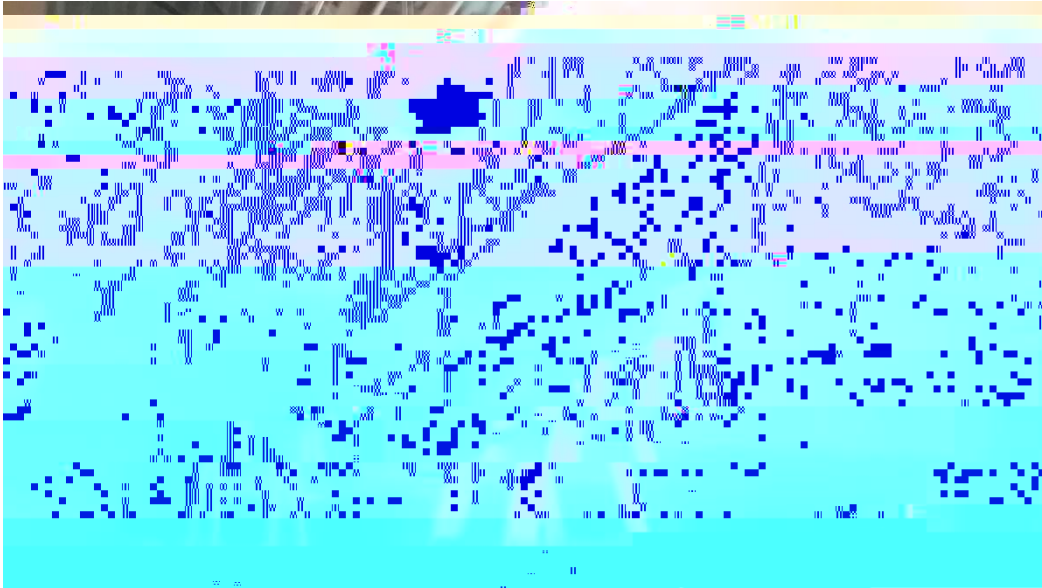


Kitchen: hood light inspection complete, as duct install to hood is completing.
Equipment is scheduled for delivery install


FIELD REPORT

PROJECT: Leavelle McCampbell Middle **FIELD REPORT NO.:** Eighty-Six (86)

CONTRACT: Construction Management @ Risk **ARCHITECTS**
HG Reynolds **PROJECT NO.:**

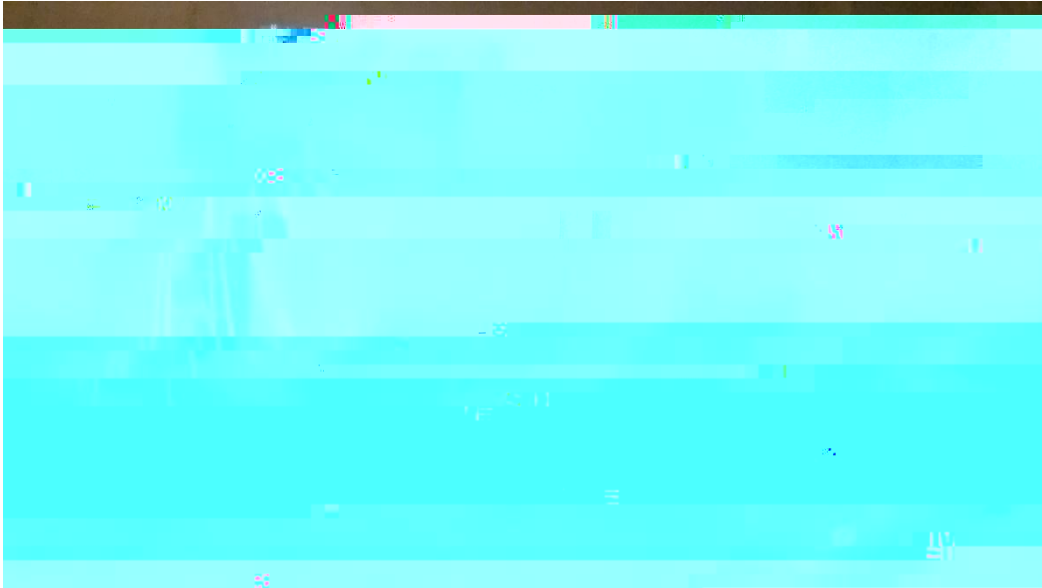

Kitchen area painted where service line area and equipment ready for placement.
Floor tile is installed and covered for protection by contractor.

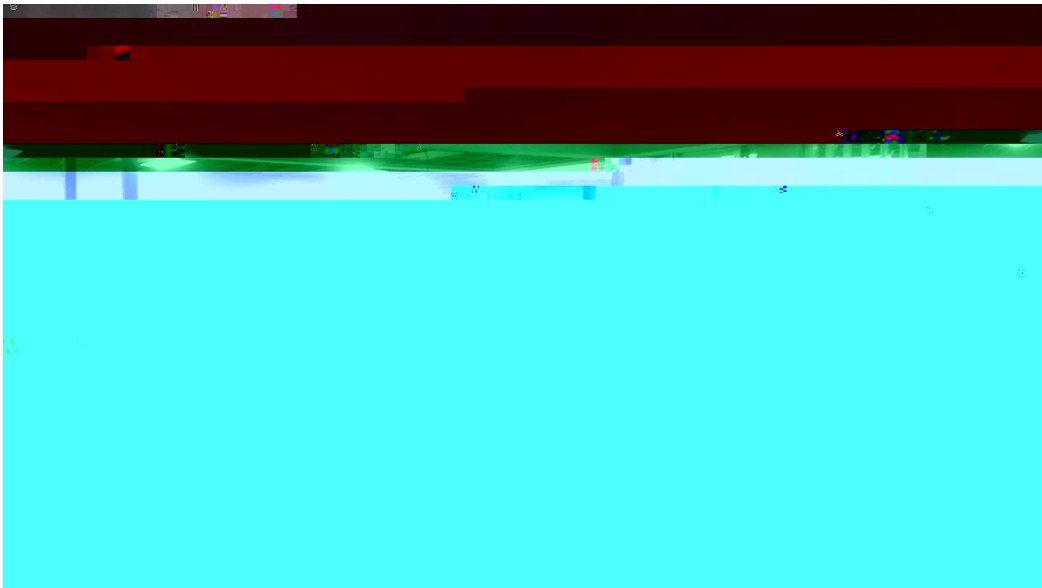

Cafeteria paint prep and finishes are ongoing and stored light fixture scheduled to install.

FIELD REPORT

PROJECT: Leavelle McCampbell Middle **FIELD REPORT NO.:** Eighty-Six (86)

CONTRACT: Construction Management @ Risk **ARCHITECTS**
HG Reynolds **PROJECT NO.:**



See ready for paint administration and main lobby entrance.

Report by: Wayne Jr. -WCI Group
