

**FIELD REPORT**

**PROJECT:** Leavelle McCampbell Middle **FIELD REPORT NO.:** One Hundred-Six (106)

**CONTRACT:** Construction Management @ Risk **ARCHITECTS**  
HG Reynolds **PROJECT NO.:**

**DISTRIBUTION:** **Owner:** Dr. Shawn Foster, Aiken County Schools  
Mr. Kevin Chipman, Aiken County Schools  
Ms. Michelle Padgett, Aiken County Schools  
Ms. Beth Clark, Aiken County Schools  
Mr. Kip Gunter, Aiken County Schools  
Ms. Sandra Waddell, Aiken County Schools  
Mr. Jeremiah Jones, Aiken County Schools

**Architect:** Mr. Donnie Love, McMillan Pazdan Smith  
Mr. Bill Williams, WCI  
Mr. Robert Wayne, WCI

**Consultant:** Mr. Mayhar Angooraj, BGA  
Mr. William Wafer, BGA  
Mr. Dan Reider, BGA

**Contractor:** Mr. Tilden Hilderbrand, Hass & Hilderbrand  
Mr. Jeffrey Reynolds, HG Reynolds  
Mr. Robert Lowe, HG Reynolds  
Mr. Graham Reynolds, HG Reynolds

**DATE:** April 20, 2017 **WEATHER:** 69 / Partly Cloudy / Breezy

**TIME:** 9:30 am **SCHEDULE** On Schedule

**COMMENTS:**

**PRESENT AT SITE:**

HG Reynolds, Fire Sprinkler HVAC, Plumbing, Electrical, Drywall, Roofing, Insulation, Paint, Flooring  
Data, Fire Alarm & Security, United AV

**OBSERVATION:**

- 1) WCI, CCI onsite for Fire Alarm System, including smoke detector and fire Sprinkler Riser Rooms, PIV Apparatus. Flow tests were conducted and satisfied. strobe lights and devices were also inspected. Inspection report has been documented and stored as required for final OSF Inspection.
- 2) GC site and coordination scope of work continues as OSF punch list work continues final as scheduled.
- 3) Installation of gym floors is complete with manufacturer installation specifications as bleacher installation is complete.
- 4)

FIELD REPORT

---

<b><u>PROJECT:</u></b>	Leavelle McCampbell Middle	<b><u>FIELD REPORT NO.:</u></b>	One Hundred-Six (106)
<b><u>CONTRACT:</u></b>	Construction Management @ Risk HG Reynolds	<b><u>ARCHITECTS</u></b> <b><u>PROJECT NO.:</u></b>	

---

**SUBMITTALS:**

- 1) PVC Pediment-Resubmitted
- 2) RONCO re-submittal

**COORDINATION:**

- 1) Bi-

FIELD REPORT


---

<b><u>PROJECT:</u></b>	Leavelle McCampbell Middle	<b><u>FIELD REPORT NO.:</u></b>	One Hundred-Six (106)
<b><u>CONTRACT:</u></b>	Construction Management @ Risk HG Reynolds	<b><u>ARCHITECTS PROJECT NO.:</u></b>	

---



Gymnasium athletic locker room and setup continues.

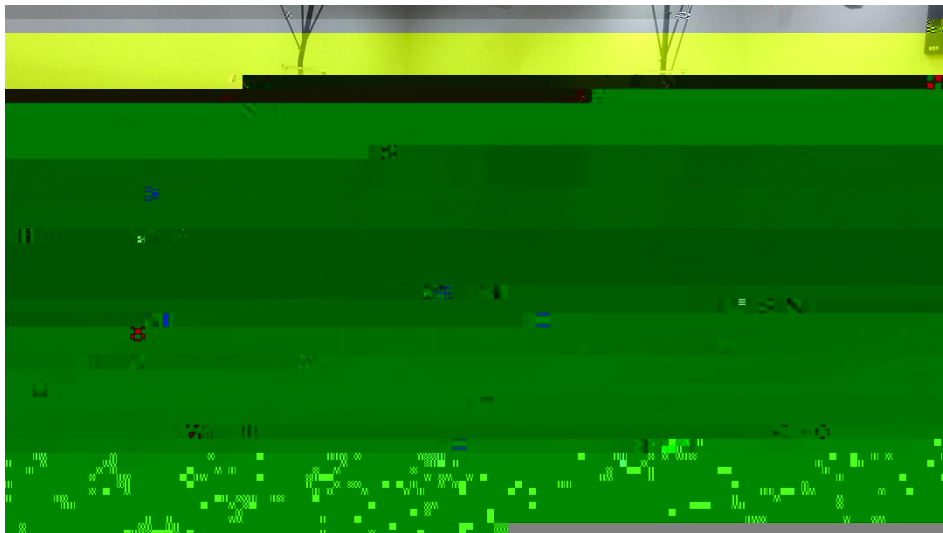

Gymnasium Floors are now complete as drying continues.

FIELD REPORT

---

<b><u>PROJECT:</u></b>	Leavelle McCampbell Middle	<b><u>FIELD REPORT NO.:</u></b>	One Hundred-Six (106)
<b><u>CONTRACT:</u></b>	Construction Management @ Risk HG Reynolds	<b><u>ARCHITECTS</u></b> <b><u>PROJECT NO.:</u></b>	

FIELD REPORT

---

PROJECT:

**McMILLAN PAZDAN SMITH**

**FIELD REPORT**


**WCI GROUP LLC**

FIELD REPORT


---

<b><u>PROJECT:</u></b>	Leavelle McCampbell Middle	<b><u>FIELD REPORT NO.:</u></b>	One Hundred-Six (106)
<b><u>CONTRACT:</u></b>	Construction Management @ Risk HG Reynolds	<b><u>ARCHITECTS PROJECT NO.:</u></b>	

---

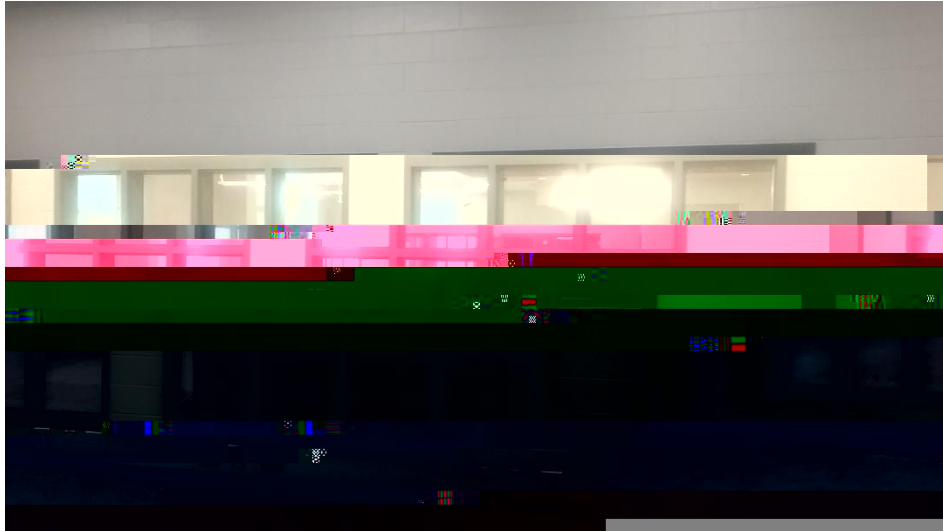

Media / Library Admin area is ready to trim out as punch work is near completion

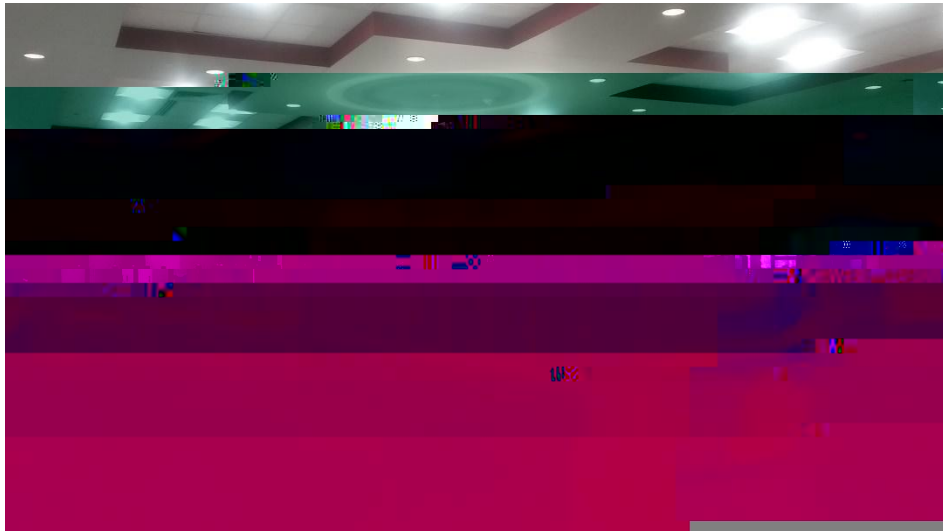

Media / Library punch out is ongoing and communication data is near completion as noted.

Report by: Wayne Jr. -WCI Group
