

FIELD REPORT

PROJECT: Leavelle McCampbell Middle **FIELD REPORT NO.:** Fifty-One (51)

CONTRACT: Construction Management @ Risk **ARCHITECTS**
HG Reynolds **PROJECT NO.:**

DISTRIBUTION: **Owner:** Dr. Shawn Foster, Aiken County Schools
Mr. Kevin Chipman, Aiken County Schools
Ms. Michelle Padgett, Aiken County Schools
Ms. Beth Clark, Aiken County Schools
Mr. Kip Gunter, Aiken County Schools
Ms. Sandra Waddell, Aiken County Schools
Mr. Jeremiah Jones, Aiken County Schools

Architect: Mr. Donnie Love, McMillan Pazdan Smith
Mr. Bill Williams, WCI
Mr. Robert Wayne, WCI

Consultant: Mr. Mayhar Angooraj, BGA
Mr. William Wafer, BGA
Mr. Dan Reider, BGA

Contractor: Mr. Tilden Hilderbrand, Hass & Hilderbrand
Mr. Jeffrey Reynolds, HG Reynolds
Mr. Robert Lowe, HG Reynolds
Mr. Graham Reynolds, HG Reynolds

DATE: Aug. 18, 2016 **WEATHER:** Sunny / 99 / Humid

TIME: 2:30 pm **SCHEDULE** On Schedule

COMMENTS:

PRESENT AT SITE:

HJR General Contractor, HVAC, Plumbing, Electrical, Masonry, Roofing, Insulation

OBSERVATION:

- 1) Site conditions are dry as masonry veneer continues progress aggressively. The Contractor (Masonry) is continues @ approximately (99%) on 3 sides with moisture barrier and brick veneer install is continuous at front façade. Masonry contractors work is consistent.
- 2) CMU Point work is aggressive and ongoing.
- 3) Roofing contractor work is aggressive and is consistent as flash of penetration for roof top curbs, devices and / or structures is ongoing and / or protected. Roof install inspections are current.
- 4) Roof Contractor has install specified roof hatch. Roof hatch is in use.
- 5) First floor HVAC duct, gas, domestic water lines progress is continuous and consistent, as prime mastic seal and seismic fastener application are continuous and as specified in corridors, gym and cafeteria is continuous as inspections are current.
- 6) Second Floor HVAC duct, gas, domestic water lines progress as install is consistent, and scheduled for inspection Monday 8/22/2016 for seal prime mastic and seismic fastener application are continuous and as specified in corridors.
- 7) Fire sprinkler riser rooms and progressing as contractors nears (75%) install at riser rooms
- 8) CCI inspection are coordinated by WCI Group as required by jobsite and consistent and documented.
- 9) The

FIELD REPORT


PROJECT: Leavelle McCampbell Middle **FIELD REPORT NO.:** Fifty-One (51)

CONTRACT: Construction Management @ Risk **ARCHITECTS**
HG Reynolds **PROJECT NO.:**

FIELD REPORT

PROJECT: Leavelle McCampbell Middle **FIELD REPORT NO.:** Fifty-One (51)

CONTRACT: CoQ2tru72 72Ma 72gement @Rsk **ARCHITECTS**
HG Rey 72s **PROJECT NO.:**

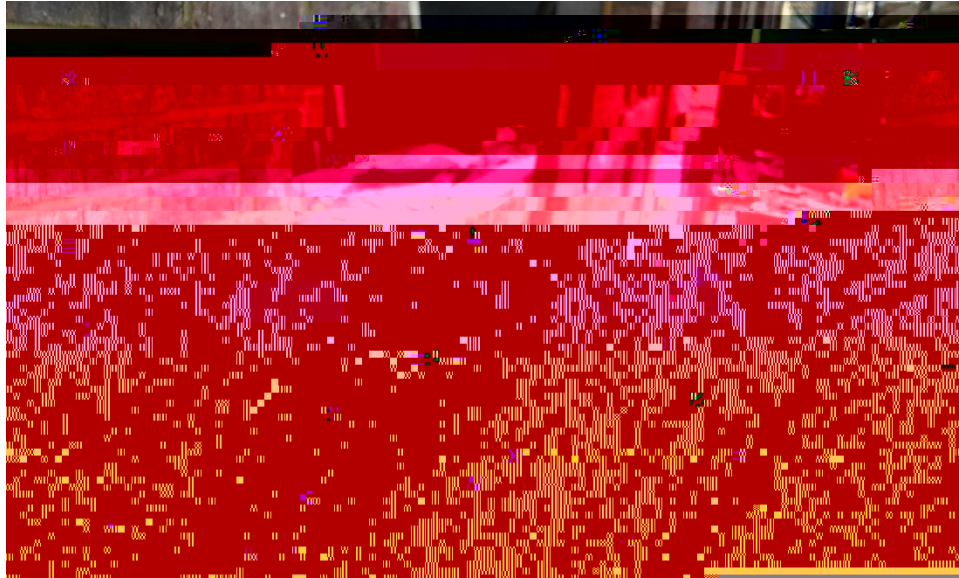

View from classroom at Maso 72y Veneer where recess accent can be viewed best



Typical Maso 72y Veneer with accent area near window

FIELD REPORT

PROJECT: Leavelle McCampbell Middle **FIELD REPORT NO.:** Fifty-One (51)

CONTRACT: Construction Management @ Risk **ARCHITECTS**
HG Reynolds **PROJECT NO.:**



Interior look at classroom (Typ.) where matching door and window frames are used



Roof Hatch view installation. Hatch is in use.

Reported by: Wayne Jr. -WCI Group
